


ID	Task Name	Duration	Start	Finish	Notes	2019	'19	'20	'21	'22	'23	2024	'24	'25
1	FIRE STATION 25	1117 days?	Fri 2/5/21	Mon 2/26/24										
2														
3	Funding	19 days	Fri 2/5/21	Tue 2/23/21										
4	BAR	19 days	Fri 2/5/21	Tue 2/23/21										
5	County prepares BAR / Submits to CMO	0 days	Fri 2/5/21	Fri 2/5/21										
6	BCC (regular meeting) to approve BAR	1 day	Tue 2/23/21	Tue 2/23/21										
7														
8	(Architectural & Engineering Services)	540 days?	Wed 2/24/21	Wed 8/17/22	18-Months									
9	Procurement	150 days	Wed 2/24/21	Fri 7/23/21	5-Months									
10	Procurement	150 days	Wed 2/24/21	Fri 7/23/21										
11	Design Phase	300 days	Fri 7/23/21	Thu 5/19/22										
12	Notice to Proceed	0 days	Fri 7/23/21	Fri 7/23/21										
13	Kick-Off Meeting	0 days	Fri 7/23/21	Fri 7/23/21										
14	Pre-Design Planning	30 days	Sat 7/24/21	Sun 8/22/21	1-Month									
15	Consultant produces Conceptual Design / Master Plan	30 days	Sat 7/24/21	Sun 8/22/21										
16	Schematic Design Phase	60 days	Mon 8/23/21	Thu 10/21/21	2-Months									
17	Consultant produces Schematic Design documents	60 days	Mon 8/23/21	Thu 10/21/21										
18	Design Development Phase	90 days	Fri 10/22/21	Wed 1/19/22	3-Month									
19	Consultant produces Design Development documents	90 days	Fri 10/22/21	Wed 1/19/22										
20	Construction Documents Phase	120 days	Thu 1/20/22	Thu 5/19/22	4-Months									
21	Release for Permit at 90%	90 days	Thu 1/20/22	Tue 4/19/22										
22	Consultant produces Construction Documents	30 days	Wed 4/20/22	Thu 5/19/22										
23														
24	Permitting	120 days?	Wed 4/20/22	Wed 8/17/22	4-Months									
25	Building Permit	120 days	Wed 4/20/22	Wed 8/17/22										
26														
27	(Construction Services)	558 days?	Thu 8/18/22	Mon 2/26/24	18-Months									
28	Procurement	150 days?	Thu 8/18/22	Sat 1/14/23	5-Months									
29	Solicitation to Award	150 days	Thu 8/18/22	Sat 1/14/23										
30														
31	Construction Phase	365 days?	Fri 1/27/23	Sat 1/27/24	12-Months									
32	Kick-Off Meeting	0 days	Fri 1/27/23	Fri 1/27/23	2-Weeks after Award									
33	Notice to Proceed	0 days	Wed 2/1/23	Wed 2/1/23	1-Week after Kick-Off									
34	Construction Phase to Substantial Completion	360 days	Thu 2/2/23	Sat 1/27/24										
35														
36	Final Completion	30 days	Sun 1/28/24	Mon 2/26/24	1-Month									
37	Final Completion (30 Calendar Days)	30 days	Sun 1/28/24	Mon 2/26/24										
38	Project Complete	0 days	Mon 2/26/24	Mon 2/26/24										

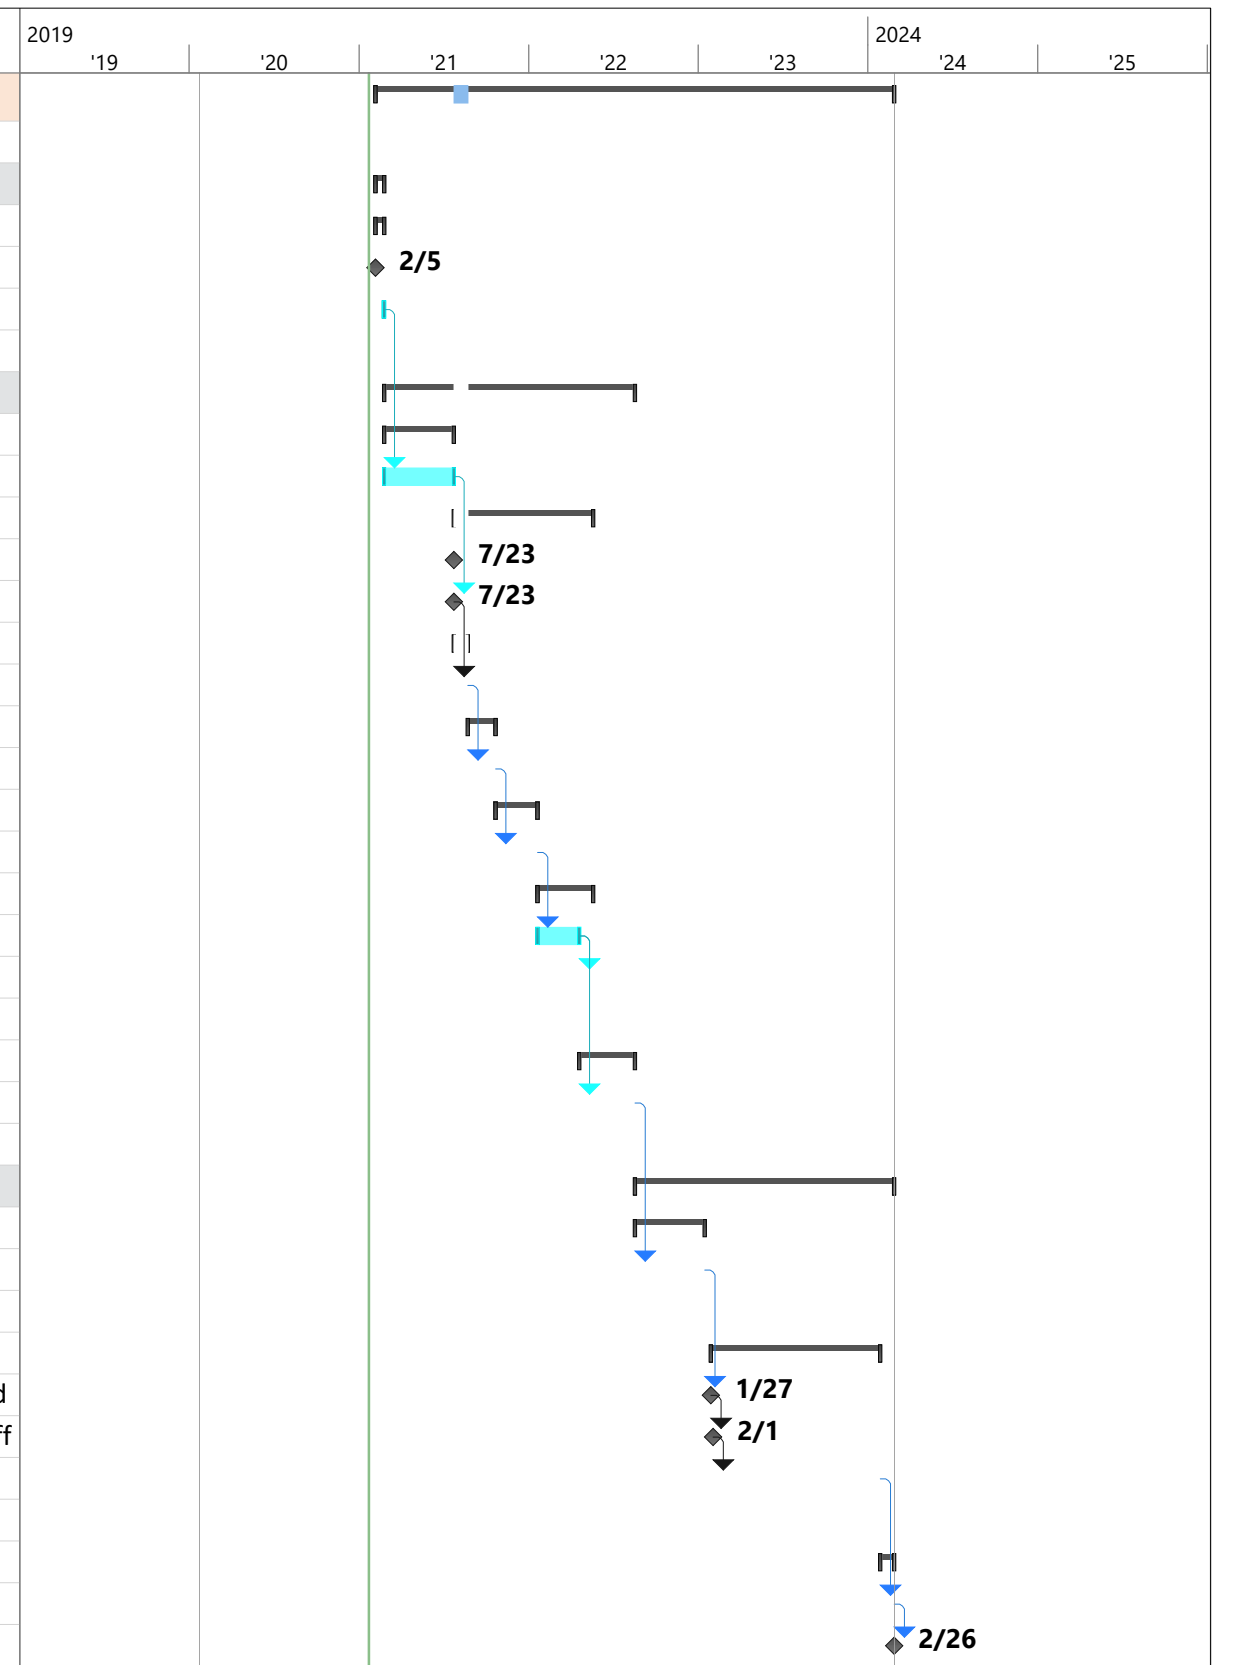

Project: 20210122_FS-25_Sched Date: Fri 1/22/21	Task	Project Summary	Manual Task	Start-only	Deadline
	Split	Inactive Task	Duration-only	Finish-only	Progress
	Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
	Summary	Inactive Summary	Manual Summary	External Milestone	
